



# CLME+ Project

Caribbean & North Brazil Shelf Large Marine Ecosystems

CLME+ PSC Meeting 11-12 October, 2021






## Agenda Item 4 (AOB): Final CLME+ Implementation Status



*Catalyzing implementation of the Strategic Action Programme for the Caribbean and North Brazil Shelf LME's*

# Financial implementation - GEF CLME+ Project budget

As of September 2021, the PCU had disbursed 99% (US\$ 12.33 MM) of the full GEF CLME+ grant (US\$ 12.5MM). Remaining payments are expected to further increase expenditures with ± 150K before project end.

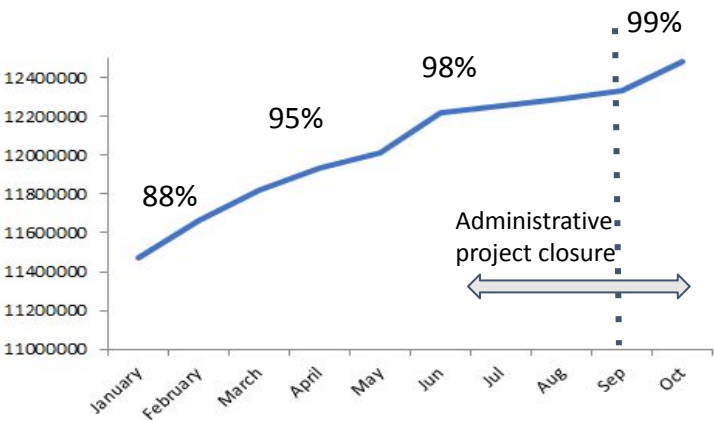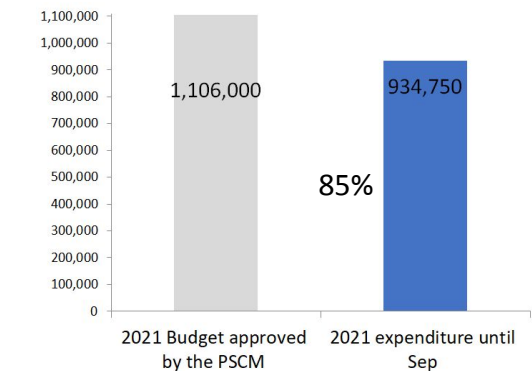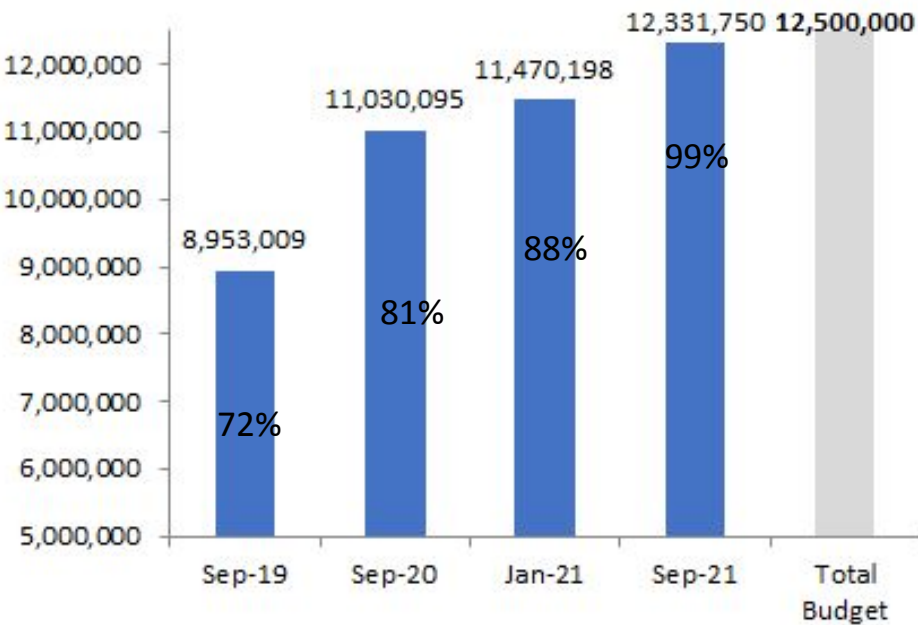

## Revised Feb PSCM work plan → *main activities undertaken*

SELECTED KEY ACTIVITIES/OUTPUTS					FINAL PROPOSAL OCT20 PSCM											
	2020				2021											
	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
CLME+ Full-Sized Project lifespan	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
CLME+ Main Implementation Period	e	e	e	e	e	e	e	e	e	e						
CLME+ Administrative Closure Period												e	e	e		
CLME+ Steering Committee Meeting (SCM)												e				
CLME+ Terminal Evaluation	e	e	e	e	e	e										
Interim Fisheries Coordination Mechanism	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
Permanent Fisheries Coordination Mechanism	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
CLME+ SAP Interim Coordination Mechanism	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
CLME+ Partnership	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
long-term "PROCARIBE" OG Coordination Mechanism	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
Sust financing plan RGF	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
CEA UN Environment	e	e	e	e	e	e	e	e	e	e						
NBSLME EBM Sub-Project	e	e	e	e	e	e	e	e	e	e						
CEA FAO	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
Shrimp & Groundfish Sub-Project	e	e	e	e	e	e	e	e	e	e						
CLME+ SOMEE and SAP M&E + online SOMEE	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
Data arrangements for SOMEE + SAP M&E (O1.4)	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
"Private Sector" Engagement	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
Communication & KM Strategy (HUB)	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
Experience Notes & Final Reporting (PCU/CERMES)	e	e	e	e	e	e	e	e	e	e	e	e	e	e		
Resource mobilization (PIF DEVELOPMENT GEF7 - PROCARIBE+)	e	e	e	e	e	e	e	e	e	e	e	e	e	e		

- Extension of project duration till **31 Oct 21** 🍌
- July - August: focus on **Admin Project Closure**
- Request for **last Special PSC Meeting: finalize MOU**
  - Requested for May
  - Planned for June
  - Postponed till 11-12 October
- PCU continued to **support IFCM, ICM** - [click here for more info](#)
- PCU continued to **support efforts towards Ocean CM MOU**
- PCU **successfully submitted PROCARIBE+ PIF** to GEF
- FAO and UNEP finalized work under their subprojects/CEA's
- SOMEE building blocks → brought online on [CLME+ Hub](#)
- Continued work on [SAP MnE Portal](#) → [CLME+ Hub](#)
- [Baseline of potential Blue Finance Investors \(CLME+ Vision\)](#)
- Continued work on [CLME+ Hub \(ICM KM platform\)](#)
- **Sustainability Strategies** → [I\(F\)CM](#) → OCM + [ROCARIBE+](#)
- Project video finalized → [click here](#)
- [TE finalized](#) - overall rating satisfactory, excellence in PM/M&E

## The CLME+ Project: a review of 6 years of continued contributions towards a healthier marine environment

After 6 years of implementation, the UNDP/GEF Caribbean and North Brazil Shelf Large Marine Ecosystems Project (CLME+) invites the region to review its achievements. In the own words of all its co-executing partners, the project shows its best practices and results on ocean governance, capacity building, implementation of Ecosystem-Based Management (EBM) and Ecosystem Approach to Fisheries (EAF), sustainable livelihoods, investments for the protection of the marine environment, knowledge management, and joint monitoring.

Dive with them in the following video!

<https://clmeplus.org/clme-project-6-years-of-continued-contributions-to-the-marine-environment-in-review/>



WATCH NOW

# DIVE WITH US

through 6 years of continued contributions  
towards a healthier marine environment in  
the CLME+ region

